CONCENTRATION & EXIT RISK ASSESSMENT

AWS exit risk review: demo organisation

Synthetic data for demonstration. Not a real organisation.

SCOPE
name contains 'prod'

ORGANIZATIONAL UNIT
Root

ACCOUNTS IN SCOPE
40 of 49

SPEND PERIOD
Oct 2025 to Sep 2026 (12 months, amortised)

SCANNED
Oct 24, 2026, 9:17 AM

MANAGEMENT ACCOUNT
111111111111

SCAN DEPTH
Dependency scan (resources and integrations)

EXIT TARGET ASSUMED
Microsoft Azure

1 Executive summary

BOTTOM LINE

Exit risk is Moderate. Most workloads are portable, but the size of the estate makes an exit a large programme. Cost and time are not yet estimated for your organisation: answer the delivery questions under Exit model.

Scores 39/100 by spend and 28/100 by number of accounts. Risk is concentrated: 6 accounts (36% of spend), mostly on Redshift, DynamoDB and Lambda, carry most of it, while 34 of 40 accounts (85%) are broadly portable.

Cost and time are provisional. They use default answers, not your organisation's. Answer the delivery questions (CI/CD, Terraform, team size, day rate) to estimate them for you.

WHAT WE FOUND

- **27% of spend ($2.7m a year)** runs on 19 bespoke, AWS-only services that must be re-engineered: Redshift $746k a year (1 account), DynamoDB $530k (6) and Lambda $391k (10); 16 others $1.0m.
- **Technical portability 41/100 (High difficulty):** 58% of the work is on AWS-only services; 613 integrations to rebuild; 2 of 5 critical accounts hard to move.
- **34 of 40 accounts are portable** (Low or Moderate risk). The 6 High or Critical accounts hold 36% of spend.
- **3 accounts set the pace:** data-platform-prod, cards-processing-prod and contact-centre-prod carry 57% of the spend at risk (spend x risk).
- **Spend grew 42%** from Oct 2025 to Sep 2026; High/Critical spend grew 38%, so lock-in is growing more slowly than the estate. Biggest monthly rises: EC2 +$62k, RDS / Aurora +$38k and Redshift +$23k.
- **The exit does not fit the 24-month deadline:** it takes roughly 3 to 5.5 years on default delivery answers. Start earlier, add capacity, or agree a longer transition.
- **Leaving in a hurry would still owe AWS $4m to $4.5m** in Savings Plans and reservations (the last ends Sep 2029); a planned exit lets them run off.
- **90% of the spend of 5 critical accounts** runs in Europe (London), so one regional event takes down most of it at once. Channels Card payments, Core banking, Mobile app, Payments and Shared platform share that region: no anti-affinity between them.

WHAT WE RECOMMEND

1. **Answer the delivery questions under Exit model** (CI/CD, Terraform, team size, day rate). Until then the cost and time figures use default answers, not your organisation's.
2. **Plan the hardest accounts first.** Write and test exit plans for data-platform-prod, cards-processing-prod and contact-centre-prod; they drive most of the cost and the timeline.
3. **Make portability a design criterion** for new work on Redshift, DynamoDB and Lambda: prefer the open-standard alternative in Appendix A unless the business case says otherwise.
4. **Pre-build a stressed-exit fallback** for the 24% of critical spend on AWS-only services: a stand-in process, a manual workaround or a warm copy elsewhere, tested before it is needed.
5. **Keep commitments inside the exit window:** a 3-year Savings Plan or reservation bought after Mar 2027 would outlast the fastest exit; after that, buy 1-year terms.

Confidence: Low

Synthetic demo data. Cost and time use default delivery answers, not yours. The deep scan reached accounts with 76% of spend. 1 service not in the catalog (0.1% of spend), scored as tier 3.

To raise confidence


1. Scan your own organisation.
2. Answer the delivery questions under Exit model (about ten minutes).
3. Deploy the ExitRiskReadOnly role to the accounts the deep scan could not reach (Issues lists them), then run a new deep scan.
4. Add the missing services to the service catalog (Appendix A lists them).

KEY FIGURES

OU exit-risk score

By spend	By no. of accounts
39/100	28/100
Moderate	Moderate

Risk is concentrated in a few large accounts: most accounts are easier to move than the spend view suggests.



Annual spend in scope
$9.9m
$828k / month, amortised

High/Critical spend
27%
$2.7m a year

Accounts in scope
40
40 with spend · 9 filtered out

High/Critical accounts
6 of 40
36% of spend · 34 portable (Low/Moderate)

AWS-only services
19
largest: Redshift, DynamoDB, Lambda

Spend growth
+41.5%
Oct 2025 → Sep 2026 · High/Critical +38.5%

Exit cost (one-off)
$9m to $18m PROVISIONAL
90 to 200% of a year's AWS spend

Exit window (time to leave AWS)
3 to 5.5 years PROVISIONAL
bound by team capacity

Engineering effort
35 to 70 person-years PROVISIONAL
team of 15 full-time people

Commitments written off
None PROVISIONAL
all end before the fastest exit finishes

WHERE THE WORK IS ● DEPENDENCY SCAN (RESOURCES AND INTEGRATIONS)

The score above weighs exit risk by spend: financial exposure. These measures weigh it by the engineering work instead, so a small but deeply wired service counts for what it takes to move.

Technical portability

41/100

High exit difficulty · weighted by effort, not spend

Exit effort

9,000 to 16,000 engineer-days PROVISIONAL

sized 43% from counted resources, 6% integrations, 51% from spend

Exit window

3 to 5.5 years PROVISIONAL

bound by team capacity

1 Service portability

41/100

58% of the work is on High or Critical (AWS-only) services

Service catalog tiers, weighted by engineering effort rather than spend

2 Dependency complexity

613 integrations

most: Step Functions to Lambda (200), API Gateway to Lambda (162); 9 accounts scanned

Declared configuration: event source mappings, rule targets, subscriptions, API integrations, workflow tasks

3 Data gravity

2,742 TB to move

47 TB in DynamoDB, 890 TB in critical accounts

Cost Explorer storage usage (GB-months); no data is read

4 Engineering effort

9,000 to 16,000 engineer-days

43% sized from counted resources, 6% integration redesign, 51% sized from spend

Resource inventory where deep-scanned, otherwise the catalog sized by spend

5 Operational criticality

5 critical accounts

Least ready: cards-processing-prod (hard to move)

Account tags or your list; a business judgement, not inferred from resources

Critical accounts: ready to move?

Judged on their own, so many easy moves elsewhere cannot hide one that is hard. Ready: portability 60 or more and no Critical services to replace.

Account	Readiness	Portability	Engineer-days	Integrations	Data	What blocks it
cards-processing-prod $101k/month	Hard to move	24	1,444	536	163 TB	DynamoDB
digital-channels-prod $57k/month	Needs work	40	450	8	85 TB	Cognito, AppSync, Pinpoint
payments-core-prod $116k/month	Hard to move	58	328	2	216 TB	DynamoDB
identity-prod $7.9k/month	Ready	77	51	n/a	n/a	none
core-banking-prod $122k/month	Ready	81	164	0	115 TB	none

AWS-specific integrations

613 found in 9 dependency-scanned accounts, 605 involving High or Critical services. Each one is wiring an exit must rebuild, whatever the services cost.

Integration	Count	Exit tier
Step Functions to Lambda	200	High
API Gateway to Lambda	162	High
Step Functions to DynamoDB	100	Critical
SQS to Lambda	58	High
DynamoDB to Lambda	28	Critical
EventBridge to Lambda	27	High
Kinesis to Lambda	22	High
EventBridge to Step Functions	8	High

Read from: API Gateway integrations (apigateway:GET); EventBridge rule targets (events:ListTargetsByRule); Lambda event source mappings (lambda:ListEventSourceMappings); SNS subscriptions (sns:ListSubscriptions); Step Functions task states (states:DescribeStateMachine; definitions are not stored). Not visible to this scan: SDK calls made inside code (for example a function writing to DynamoDB); S3 event notifications and Lambda resource-policy triggers; network traffic between workloads (VPC Flow Logs, X-Ray or OpenTelemetry would show it). Missing evidence is not evidence of independence.

2 Agentic Risk Review

An AI model reads the whole report in three passes (every material account, the whole estate, then an independent consistency review) and gives a second opinion: what matters most, which accounts to focus on and how to tackle them. Optional; the report's own figures do not change.

Not run for this report

The Agentic Risk Review is optional: an AI second opinion on what matters most, the accounts to focus on and how to tackle them. Tick it in New scan, or run it on the report in the console.

3 Where the exit risk sits

Monthly spend by exit-risk tier


Share of in-scope spend by how hard it is to move.



Tier	Per month	Share	Services	Accounts
1 · Portable	$288k	34.8%	12	35
2 · Low	$245k	29.6%	18	39
3 · Moderate	$70k	8.5%	11	7
4 · High	$159k	19.2%	16	14
5 · Critical	$66k	7.9%	3	7

Spend trend by tier

Is lock-in growing? Monthly amortised spend.

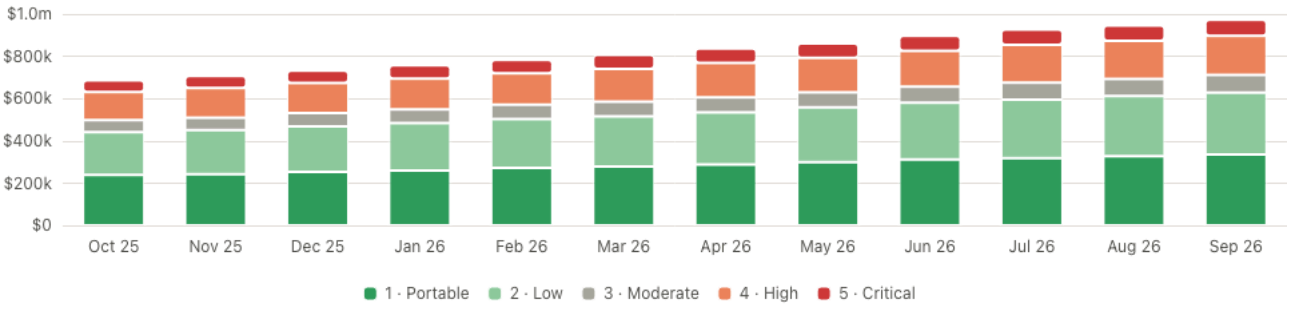


SPEND GROWTH BY PRODUCT TYPE

Oct 2025 to Sep 2026: total spend +41.5% (+46.0% a year); spend on High/Critical services +38.5% (+42.6% a year). Lock-in is growing more slowly than the estate.

Change in monthly spend

Change in monthly spend from Oct 2025 to Sep 2026, by product type, in dollars and percent. Under each type, the service that moved most. Each bar is split by how hard its services are to exit: green easy, grey moderate, red hard.

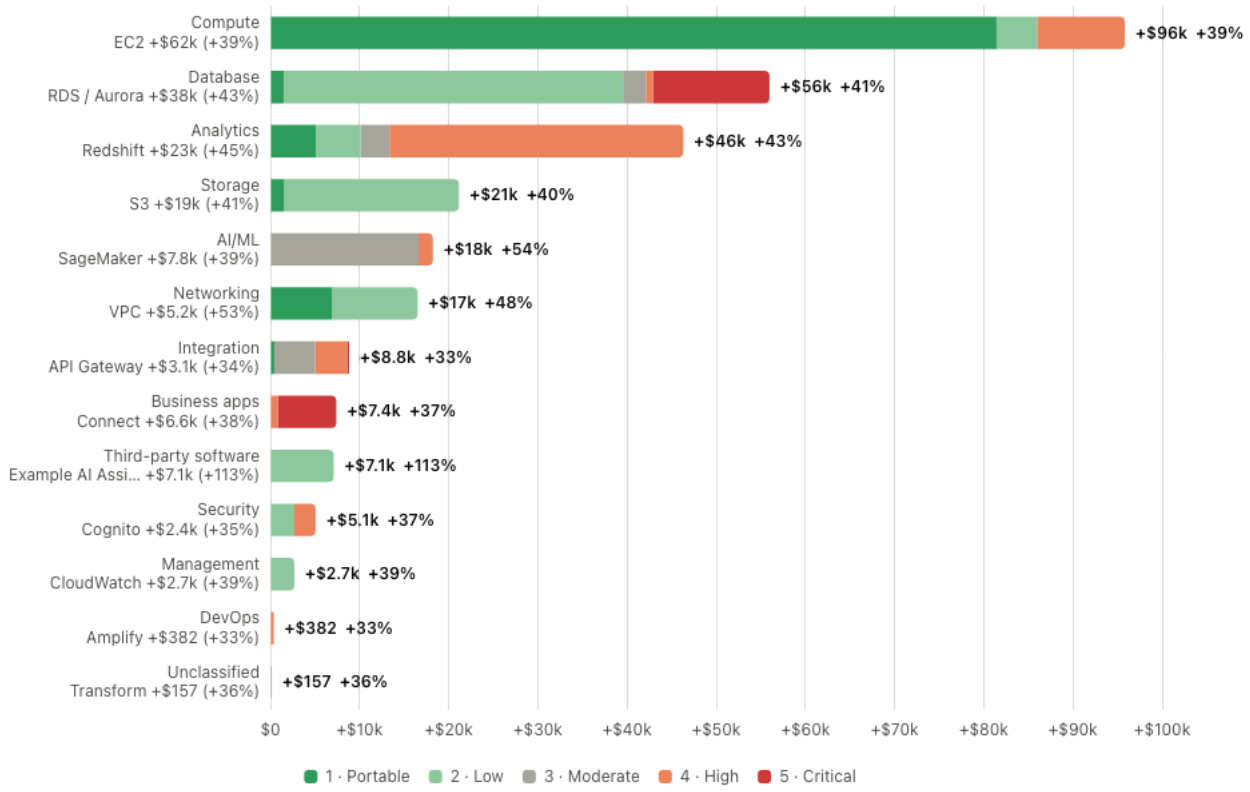

Monthly spend by product type


Product type	Oct 2025	Sep 2026	Change	Per year	Lock-in
Compute EC2, EC2 Other (EBS, NAT, transfer), Lambda, ECS +2 more	$247k	$343k	+38.8%	+43.0%	11%
Database RDS / Aurora, DynamoDB, Neptune, ElastiCache +1 more	$137k	$193k	+40.8%	+45.2%	28%
Analytics Redshift, Glue, EMR, Kinesis Streams +9 more	$108k	$154k	+43.1%	+47.8%	71%
Storage S3, FSx, Backup	$54k	$75k	+39.5%	+43.8%	0%
AI/ML SageMaker, Bedrock, Transcribe, Lex +2 more	$34k	$52k	+54.2%	+60.4%	10%
Networking VPC, Direct Connect, CloudFront, Network Firewall +3 more	$34k	$51k	+47.9%	+53.3%	0%
Integration API Gateway, Step Functions, AppSync, SQS +4 more	$27k	$36k	+32.8%	+36.3%	45%
Business apps Connect, Pinpoint	$20k	$27k	+37.2%	+41.2%	100%
Security Cognito, KMS, Directory Service, ACM / Private CA +2 more	$14k	$19k	+36.8%	+40.7%	49%
Third-party software Marketplace (3rd party)	$6.3k	$13k	+112.5%	+127.5%	0%
Management CloudWatch	$7.0k	$9.7k	+38.6%	+42.8%	0%
DevOps Amplify	$1.1k	$1.5k	+33.4%	+36.9%	100%
Unclassified Transform	$435	$592	+36.0%	+39.9%	0%
Total	$689k	$974k	**+41.5%**	+46.0%	

Per year = the first-to-last-month change annualised. Amortised spend: Savings Plans and RIs are spread over the months they cover.

4 Accounts: how many are at risk, and how big

Accounts by exit-risk rating

Share of accounts (top) against share of spend (bottom). Few accounts holding a lot of spend is a concentration to manage, not an estate-wide problem.

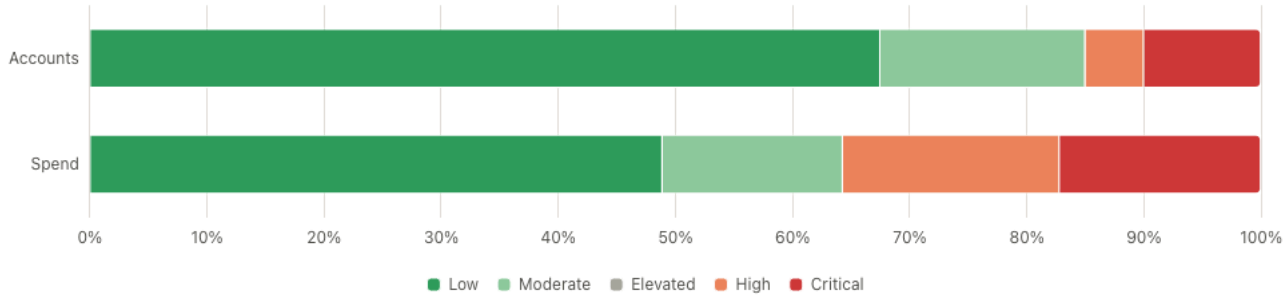


Portable vs higher-risk accounts

Rating	Accounts	Share	Per month	Spend share
Low	27	67.5%	$405k	48.9%
Moderate	7	17.5%	$128k	15.4%
Elevated	0	0.0%	$0	0.0%
High	2	5.0%	$153k	18.5%
Critical	4	10.0%	$142k	17.2%
Portable (Low + Moderate)	**34**	85.0%		

OU score weighting: By spend. Each account counts in proportion to its spend, so a small high-risk account adds little. It sets bubble sizes and contributions; change it in the bar at the top.

Inherent risk vs spend

Each bubble is an account. Up = harder to move; right = bigger; bubble size = points it contributes to the OU score. Top-right accounts drive the exit.

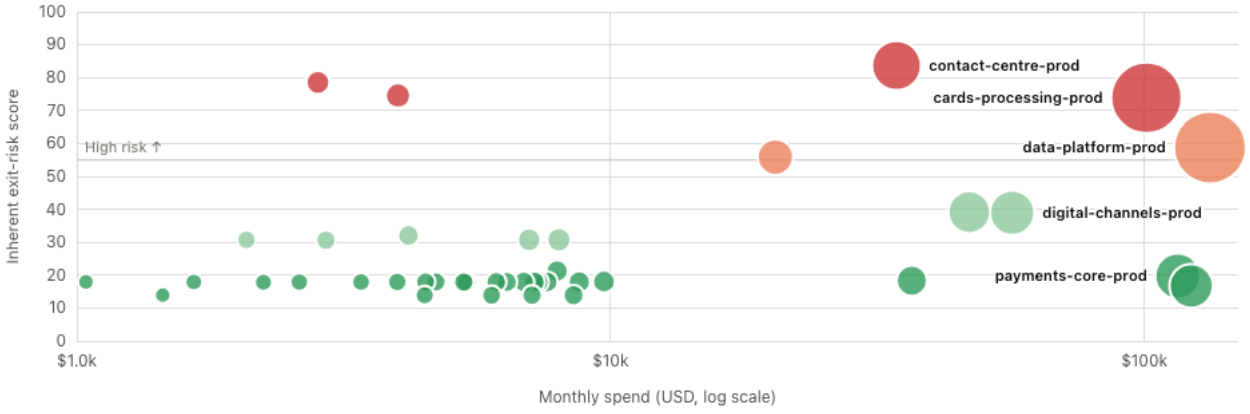

Account ranking by criticality: spend × risk

Most common lock-in: Lambda 10 · DynamoDB 5 · QuickSight 2

#	Account	Per month	Risk	Spend at risk / month	Main lock-in
1	**data-platform-prod** 561017993421 · Root / Workloads / Production · Owner: Emma Botha	$133k	High · 59 63% High/Crit spend	$78k	Redshift · Glue · QuickSight
2	**cards-processing-prod** Critical 966773840736 · Card payments · Root / Workloads / Production · Owner: Priya Shah	$101k	Critical · 74 77% High/Crit spend	$75k	DynamoDB · Lambda · Kines
3	**contact-centre-prod** 125285552493 · Contact centre · Root / Workloads / Production · Owner: Lerato Mokoena	$34k	Critical · 84 86% High/Crit spend	$29k	Connect · Lex · Lambda
4	**payments-core-prod** Critical 534439589175 · Payments · Root / Workloads / Production · Owner: Priya Shah	$116k	Low · 20 3% High/Crit spend	$23k	DynamoDB · Lambda
5	**digital-channels-prod** Critical 978681853473 · Mobile app · Root / Workloads / Production · Owner: Lerato Mokoena	$57k	Moderate · 39 25% High/Crit spend	$22k	Cognito · AppSync · Pinpoin
6	**core-banking-prod** Critical 813958344723 · Core banking · Root / Workloads / Production · Owner: Thabo Dlamini	$122k	Low · 17 0% High/Crit spend	$21k	none
7	**ml-platform-prod** 217230843944 · Root / Workloads / Production · Owner: Emma Botha	$47k	Moderate · 39 3% High/Crit spend	$18k	Bedrock AgentCore
8	**fraud-analytics-prod** 466806226017 · Root / Workloads / Production · Owner: Emma Botha	$20k	High · 56 28% High/Crit spend	$11k	DynamoDB · Timestream · L
9	**shared-network-prod** 263737281768 · Root / Infrastructure	$37k	Low · 18 0% High/Crit spend	$6.7k	none
10	**search-prod** 899894212661 · Root / Workloads / Production	$4.0k	Critical · 75 70% High/Crit spend	$3.0k	DynamoDB · Lambda
11	**mobile-backend-prod** 434423300025 · Root / Workloads / Production · Owner: Lerato Mokoena	$8.0k	Moderate · 31 15% High/Crit spend	$2.5k	Lambda
12	**treasury-reporting-prod** 499647302627 · Root / Workloads / Production · Owner: Thabo Dlamini	$2.8k	Critical · 79 92% High/Crit spend	$2.2k	DynamoDB · QuickSight · La
13	**merchant-portal-prod** 386906790760 · Root / Workloads / Production	$7.0k	Moderate · 31 15% High/Crit spend	$2.2k	Lambda
14	**doc-store-prod** 454519794043 · Root / Workloads / Production	$9.7k	Low · 18 0% High/Crit spend	$1.8k	none
15	**identity-prod** Critical 189183446249 · Shared platform · Root / Infrastructure · Owner: Thabo Dlamini	$7.9k	Low · 21 0% High/Crit spend	$1.7k	none
16	**id-verify-prod** 267387487076 · Root / Workloads / Production	$8.7k	Low · 18 0% High/Crit spend	$1.6k	none
17	**payroll-api-prod** 295250496497 · Root / Workloads / Production	$7.6k	Low · 18 0% High/Crit spend	$1.4k	none
18	**legacy-batch-prod** 107537456074 · Root / Workloads / Production	$4.2k	Moderate · 32 25% High/Crit spend	$1.3k	SWF · Data Pipeline
19	**branch-queue-prod** 717640922470 · Root / Workloads / Production	$7.3k	Low · 18 0% High/Crit spend	$1.3k	none
20	**insurance-quotes-prod** 498633168856 · Root / Workloads / Production	$7.2k	Low · 18 0% High/Crit spend	$1.3k	none
21	**disputes-prod** 844781801768 · Root / Workloads / Production	$6.9k	Low · 18 0% High/Crit spend	$1.2k	none
22	**investments-prod** 514740085648 · Root / Workloads / Production	$8.5k	Low · 14 0% High/Crit spend	$1.2k	none
23	**card-controls-prod** 170174047247 · Root / Workloads / Production	$6.4k	Low · 18 0% High/Crit spend	$1.2k	none
24	**pricing-prod** 322790187289 · Root / Workloads / Production	$6.1k	Low · 18 0% High/Crit spend	$1.1k	none
25	**reporting-hub-prod** 244219422241 · Root / Workloads / Production · Owner: Emma Botha	$7.1k	Low · 14 0% High/Crit spend	$997	none

Top 25 of 40 accounts by spend at risk. The JSON export lists every account.

Who owns the risk from the accounts' owner and executive tags

Chris Ndlovu carries the most spend at risk: $109k a month across 4 accounts.


Executive or owner	Accounts	Per month	Spend at risk / month	High/Critical accounts	Account owners
Chris Ndlovu	4	$207k	$109k	2	Emma Botha
Alex Morgan	2	$216k	$97k	1	Priya Shah
Sam Patel	3	$99k	$53k	1	Lerato Mokoena
Jordan Lee	3	$133k	$25k	1	Thabo Dlamini

12 accounts of 40 with spend carry an owner or executive tag. 28 accounts ($172k a month) have none and are left out of this table.

5 Services driving lock-in

Top services by spend

Coloured by exit-risk tier.

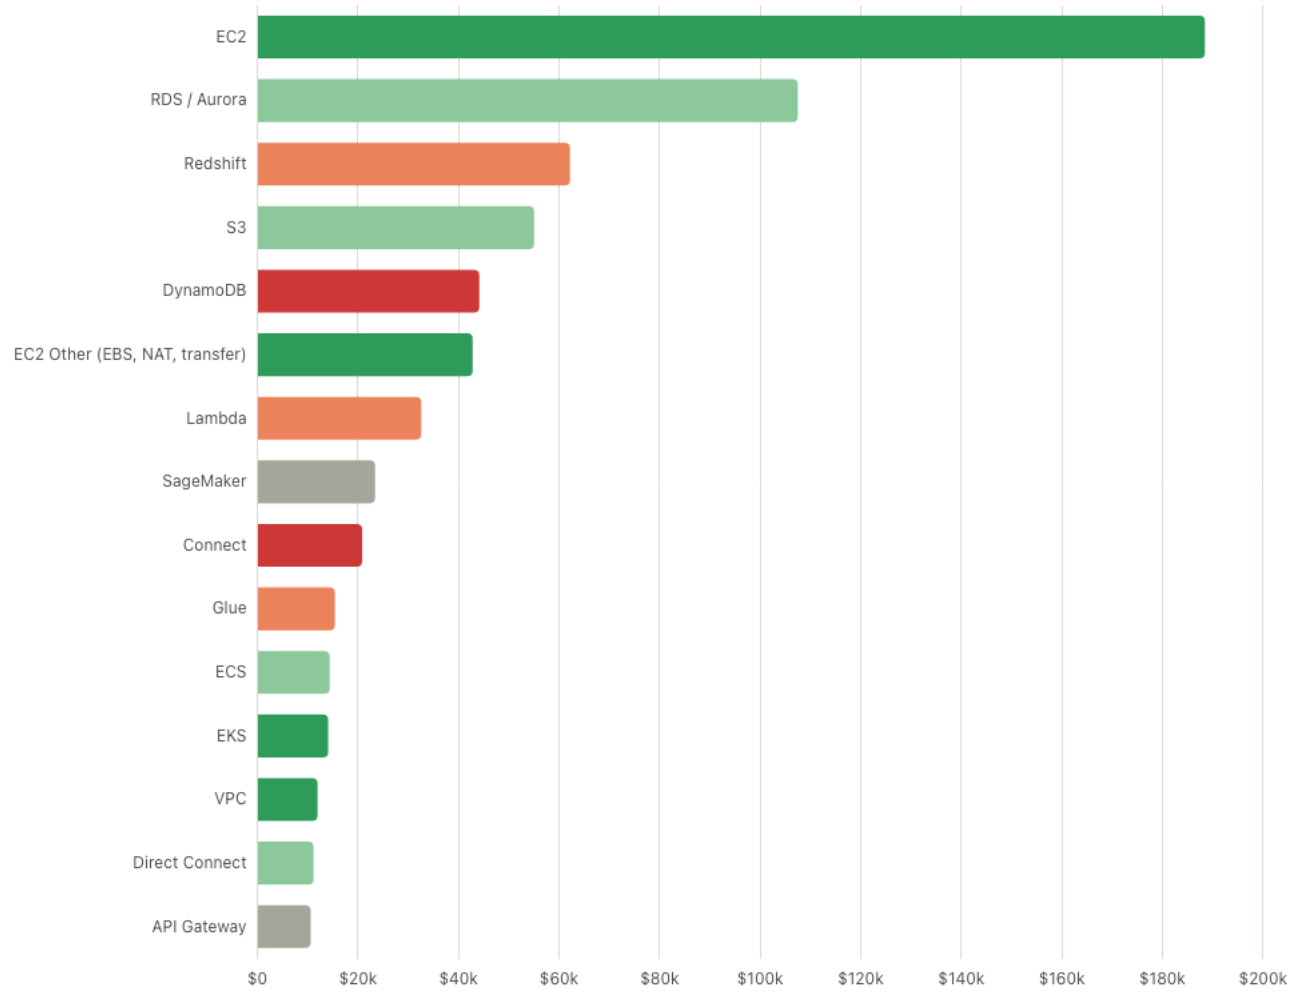

High & critical services in use

Service	Tier	Per month	Share	Accounts	Change
Redshift Analytics	4 · High	$62k	7.5%	1	+$23k +45%
DynamoDB Database	5 · Critical	$44k	5.3%	6	+$13k +35%
Lambda Compute	4 · High	$33k	3.9%	10	+$9.8k +35%
Connect Business apps	5 · Critical	$21k	2.5%	1	+$6.6k +38%
Glue Analytics	4 · High	$15k	1.9%	1	+$5.4k +42%
Kinesis Streams Analytics	4 · High	$9.7k	1.2%	2	+$2.8k +34%
Cognito Security	4 · High	$8.0k	1.0%	2	+$2.4k +35%
Step Functions Integration	4 · High	$7.4k	0.9%	2	+$1.8k +27%
QuickSight Analytics	4 · High	$5.9k	0.7%	2	+$2.0k +41%
AppSync Integration	4 · High	$4.3k	0.5%	1	+$1.3k +37%
Lex AI/ML	4 · High	$3.1k	0.4%	1	+$1.1k +44%
Pinpoint Business apps	4 · High	$2.8k	0.3%	1	+$837 +34%
Timestream Database	4 · High	$2.0k	0.2%	1	+$783 +48%
EventBridge Integration	4 · High	$1.7k	0.2%	1	+$510 +36%
Amplify DevOps	4 · High	$1.3k	0.2%	1	+$382 +33%
Bedrock AgentCore AI/ML	4 · High	$1.2k	0.1%	1	+$473 +47%
SWF Integration	5 · Critical	$712	0.1%	1	+$215 +35%
Lake Formation Analytics	4 · High	$640	0.1%	1	+$219 +42%
Data Pipeline Analytics	4 · High	$327	0.0%	1	+$86 +30%

Third-party products billed through AWS

Marketplace software and third-party models on Bedrock. Usually portable: the vendor sells direct or on other clouds, but each contract needs re-papering.

Product	Billed as	Per month	Accounts	Change
Claude Sonnet 4.6	Bedrock	$3.9k	1	+$4.9k
Example Streaming Cloud - Pay As You Go	Marketplace (3rd party)	$3.5k	1	+$1.6k
Example Observability Platform	Marketplace (3rd party)	$2.7k	1	+$2.0k
Example Data Integration Cloud	Marketplace (3rd party)	$1.7k	1	+$564
Example AI Assistant for Enterprise	Marketplace (3rd party)	$1.2k	1	+$3.0k
Claude Haiku 4.5	Bedrock	$1.1k	1	+$963

6 Exit cost & time estimate

Exit cost (one-off)

$9m to $18m PROVISIONAL

90 to 200% of a year's AWS spend · about 73% engineering, the rest parallel running and the target platform

Exit window (time to leave AWS)

3 to 5.5 years PROVISIONAL

bound by team capacity


Engineering effort

35 to 70 person-years PROVISIONAL


40 material accounts · 2.7 PB of data · narrower range: integrations counted

Commitments written off, over time

The exit finishes between Mar 2030 and Dec 2031 (shaded). Bars after the fastest finish are commitments paid for but no longer used: none written off. The red line is what would be written off if the exit finished at the end of that month. Savings Plans and reservations cover the whole organisation, even though the report is filtered (name contains 'prod').

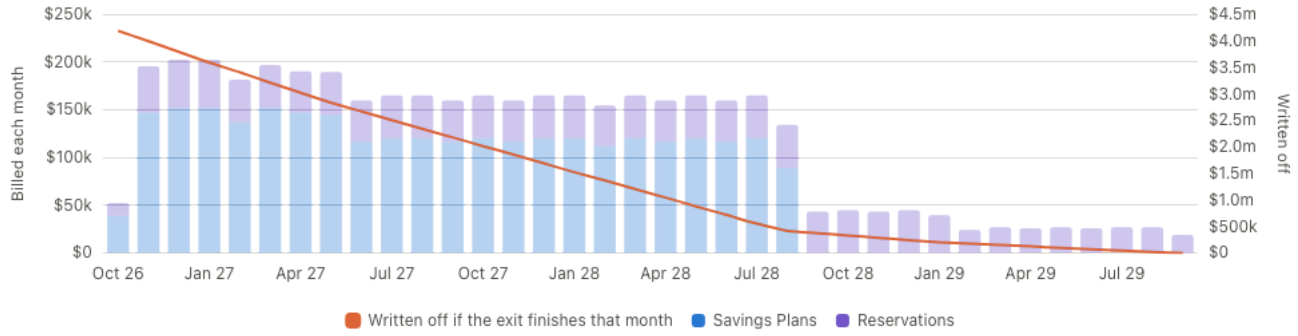


Indicative timeline

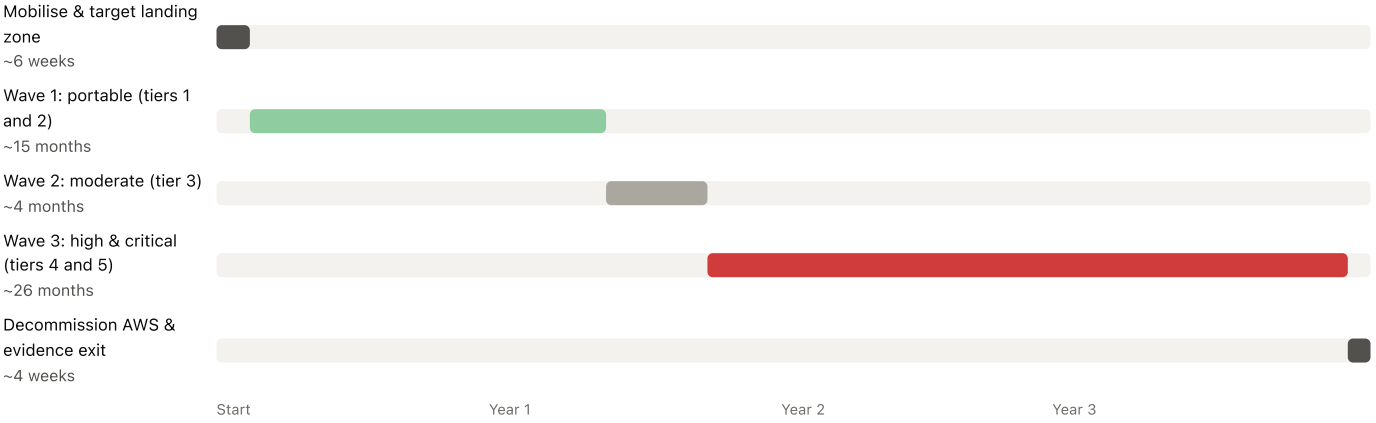

Where the effort goes

Person-months, after the delivery-maturity adjustment.

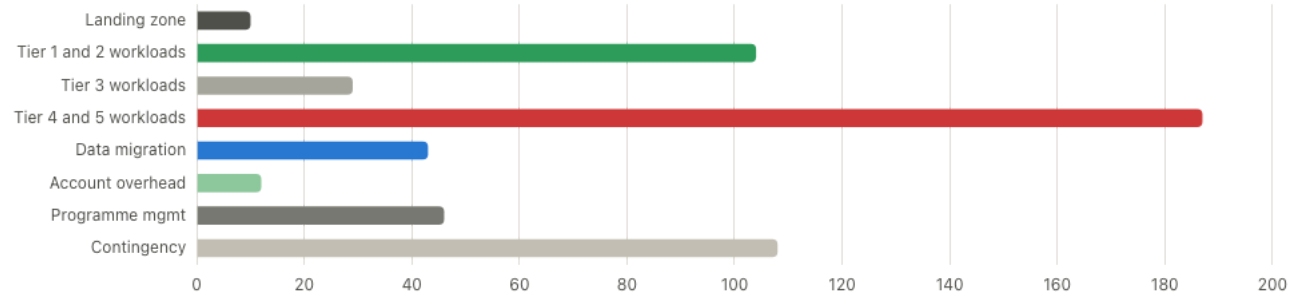

Tools that shorten the move

The 15 services with the most work, and the tools that do part of it for Microsoft Azure. Not counted in the estimate yet: tick migration tools in the Exit model once you plan to use them.

Service	Person-months	Tools	Tool help	AI agent help
Lambda	41	AI coding agents translate handlers and AWS SDK calls; Serverless Framework or SST deploy to several clouds Azure Functions Core Tools	Medium	High
RDS / Aurora	23	Native replication (PostgreSQL logical replication, MySQL binlog replication, Oracle Data Guard or GoldenGate, SQL Server Always On) for a short cutover Azure Database Migration Service	High	Low
DynamoDB	23	Export to S3 plus DynamoDB Streams for the changes since, then a bulk load Data Factory or the Cosmos DB Spark connector into Cosmos DB	Medium	Low
EC2	19	Block-level server replication copies running machines and cuts over in minutes Azure Migrate (server migration)	High	Low
Glue	18	AI coding agents port GlueContext and DynamicFrame code to plain Spark; export the Data Catalog to a Hive Metastore Databricks or Fabric Spark, Data Factory	Medium	High
Connect	17	Contact flows export as JSON for reference; the new contact-centre vendor's migration service rebuilds them Dynamics 365 Contact Center	Low	None
Step Functions	14	AI agents translate Amazon States Language definitions; Temporal or Argo Workflows as a neutral engine Logic Apps, Durable Functions	Medium	High
S3	10	rclone or MinIO Client (mc) copy and verify objects AzCopy, Azure Storage Mover, Azure Data Box for bulk	High	Low
SageMaker	7	MLflow tracks and moves models; containers and ONNX keep them portable Azure Machine Learning	Medium	Medium
EKS	7	Velero backs up and restores workloads and volumes; Helm and GitOps (Argo CD, Flux) redeploy the same manifests AKS	High	Medium
API Gateway	7	Export each API as OpenAPI and import it into the target gateway API Management OpenAPI import	Medium	High
ECS	5	Images run unchanged; AI agents convert task definitions to Kubernetes or Container Apps manifests Azure Container Apps	Medium	High
Kinesis Streams	4	Kafka Connect Kinesis source connector or Flink to bridge streams during the move Azure Event Hubs	Medium	Medium
Redshift	4	SQL translators (BigQuery Migration Service, SnowConvert, sqlglot) and AI agents for stored procedures; data unloads to Parquet Fabric Data Warehouse or Databricks SQL	High	Low
QuickSight	4	Datasets re-point; dashboards are rebuilt Power BI	Low	Medium

Your answers and the assumptions behind the estimate

Standard CI/CD pipeline Several, partially standard pipelines	Terraform / IaC Terraform with significant drift	Core cloud team 10 people at 50%	Application engineers 10 FTE
Target Microsoft Azure	Blended day rate 750 USD	Contingency 25%	Parallel running 6 months
Regulated Yes	AI coding agents Not used	Migration tools Not planned	Developer-portal templates No
Move into AWS Not given	Left out Nothing		

- Service effort, where an account was not deep-scanned: catalog engineer-weeks per workload × √(monthly spend / 1,000 USD), clamped to 0.25 to 8.0×. In material deep-scanned accounts effort comes from resource counts instead (below), so a cheap but complex service weighs more than a large portable one.
- Effort from resources (deep-scanned accounts): engineer-days per resource: EC2 instances 0.5, Lambda functions 2, DynamoDB tables 6, Step Functions state machines 4, Kinesis streams 3, SQS queues 0.5, SNS topics 0.5, EventBridge rules 1, API Gateway REST APIs 3, API Gateway HTTP APIs 2, Cognito user pools 15, Glue jobs 3, Redshift clusters 20, EKS clusters 10, ECS clusters 2, ECS services 2, S3 buckets 0.5; RDS instances 3 (open-source engine), 5 (Oracle, SQL Server, Db2), 6 (Aurora). Lambda functions on a custom runtime x1.5, on an end-of-support runtime x1.3, packaged as containers x0.7. After the first 20 of a type in an account, each further one counts 35% (repeat work). CloudFormation stacks are counted but carry no effort of their own: they package the resources above, and rewriting templates is the infrastructure-as-code factor. Uncalibrated planning assumptions: challenge them with your own migration history.
- Integration redesign (dependency scan): 1 engineer-day per AWS-specific integration (event source mappings, EventBridge targets, SNS subscriptions, API Gateway integrations, Step Functions tasks), less for e-mail, SMS and HTTP endpoints, with the same repeat discount; each counted once, so shared resources are not counted twice.
- Services under 25 USD/month in an account are scored but not estimated (immaterial); the cut-off applies per service per account.
- 1 engineer-week per material account for network, IAM and decommissioning.
- Target landing zone: 24 weeks (4 + 12 × √(spend / 100,000 USD), max 24) + 0.5 per material account.
- Delivery factor 1.26 = CI/CD 1.0 × IaC 1.1 × target 1.0 × regulated 1.15.
- Programme management and assurance 12%; contingency 25%.
- Data migration: 0.04 engineer-weeks per TB moved (change-data capture, validation, reconciliation) + 1 per account holding 1 TB or more: 2,742 TB in 38 accounts.
- Engineers are 80% productive on migration work, and the team runs at half strength for its first 12 weeks. Duration is the longest of effort ÷ capacity, the critical path of the hardest tier present, and the data path (12 weeks to order links, the bulk copy on 20 Gbps at 80%, 8 weeks of final sync and cutover), plus decommissioning.
- Parallel running: 6 months at 50% of current AWS spend (target ramps up as AWS ramps down). The target platform (landing zone, network, security tooling) runs at 2% of the AWS bill a month from the end of mobilisation to the end of the exit (46 months).
- Excluded: target-cloud run cost after exit, licence changes, AWS commitments still owed after the exit (EDP, Savings Plans, RIs; shown under Timing), and the cost of copying the data out: Direct Connect ports and data-out fees are sized under Resilience, Links for the migration. Since March 2024 AWS credits internet egress (not Direct Connect) for customers leaving AWS, on request to AWS Support and subject to approval, for a move completed within about 60 days.
- Figures are quoted as ranges, widened to round numbers: -20% / +35% on cost and effort, -15% / +30% on duration. The range narrows as the evidence improves: widest on billing data alone, narrowest once a dependency scan has counted the integrations (this report: dependency scan). The single figures are planning midpoints, not forecasts.

Timing: your deadline and AWS commitments

Notice period	EDP ends	EDP annual commit
24 months	Jun 2028	$8.0m

Exit finishes

Mar 2030 to Dec 2031 PROVISIONAL

3 to 5.5 years if it starts now

Deadline

Does not fit PROVISIONAL

24-month notice

Commitments

$199k/mo

$4.2m still to run · last ends Sept 2029

EDP

ends Jun 2028

$13.5m of commit left

- The exit does not fit the 24-month notice period: even the fast end runs over, and the slow end is 42 months over.
- Every Savings Plan and reservation ends before the fastest exit finishes, so a planned exit pays nothing to break them. Leaving in a hurry would still owe $4m to $4.5m.
- A new 3-year term bought after Mar 2027 would outlast the fastest exit; 1-year terms stay safe until Mar 2029.
- The EDP ends Jun 2028, before the exit finishes: renew on a shorter term or without a commit.

Savings Plans and reservations

2 Savings Plans and 3 reservations from Cost Explorer, amortised per month. Written off is what would still be owed between the exit finishing and the commitment ending: paid for, no longer used.

Commitment	Term	Ends	Per month	Still to run	Written off
Compute Savings Plan 97% used	3yr No Upfront	Aug 2028	$118k	$2.6m	n/a
RDS reservation 89% used	3yr All Upfront	Sept 2029	$27k	$927k	n/a
Redshift reservation 85% used	3yr All Upfront	Jan 2029	$18k	$481k	n/a
EC2 Instance Savings Plan 93% used	1yr Partial Upfront	May 2027	$31k	$217k	n/a
ElastiCache reservation 81% used	1yr No Upfront	Feb 2027	$5.2k	$21k	n/a

7 Resilience: critical accounts, data and a stressed exit

A planned exit is one question. Regulators also ask what happens to critical services if AWS, or one region, fails, and what could move in weeks rather than years. These figures inform; they do not change the score or the estimate.

Critical accounts	Direct Connect today	Carrier cost per new link
5 accounts tagged	2 × 10 Gbps	Not entered

Critical accounts
5
49% of spend · $4.8m a year

Correlated failure
High · 90
90% of critical spend in Europe (London)

No rapid exit
24%
of critical spend is on AWS-only services

Data to move
2.7 PB
13 to 52 days on 1 to 4 new 10 Gbps links

Correlated failure: where the critical estate runs


Share of critical spend by region (5 critical accounts). One regional event takes out everything in the top bar at once. A further 3.0% is global services (IAM, Route 53, CloudFront), which share a control plane across regions.



Channel	Runs mainly in	Isolated from other channels?
Card payments	Europe (London) 90%	No
Core banking	Europe (London) 90%	No
Mobile app	Europe (London) 90%	No
Payments	Europe (London) 90%	No
Shared platform	Europe (London) 90%	No

Stressed exit: what could move in a hurry

If AWS stopped serving you with little notice, how fast could critical spend ($4.8m a year) move?



Critical account with no rapid exit	Per month	AWS-only
cards-processing-prod DynamoDB, Lambda, Kinesis Streams	$101k	77%

Data held: what an exit has to move

Average data stored last month, from Cost Explorer storage usage (GB-months); no data is read. 3.3 PB in all: 2.4 PB live, 261 TB archived and 594 TB of snapshots and backups, which are rebuilt at the target rather than moved.

- 2.7 PB (live and archived) has to move; the options for the links that carry it are below.
- Over the internet instead, AWS waives data transfer out for customers leaving AWS if the move finishes within 60 days: that needs about 9 Gbps of internet capacity for two months. Without that credit, internet egress at list price would be roughly $140k to $421k.
- Critical accounts hold 890 TB: the data a stressed exit would need first.
- DynamoDB holds 47 TB; the largest account (cards-processing-prod) holds 37 TB. Exports to S3 are not region-limited, but rebuilding in a second region by import from S3 takes 38 import jobs of up to 1 TB each outside us-east-1, us-west-2 and eu-west-1.
- By region: Europe (London) 3.3 PB.

Service	Live	Archive	Copies
Simple Storage Service	1.6 PB	261 TB	n/a
Redshift	486 TB	n/a	121 TB
Relational Database Service	126 TB	n/a	262 TB
EC2 - Other	209 TB	n/a	167 TB
DynamoDB	47 TB	n/a	43 TB

Account	Live	Archive	Copies
data-platform-prod	1.1 PB	261 TB	136 TB
payments-core-prod Critical	216 TB	n/a	111 TB
core-banking-prod Critical	115 TB	n/a	143 TB
cards-processing-prod Critical	163 TB	n/a	34 TB
ml-platform-prod	123 TB	n/a	n/a
digital-channels-prod Critical	85 TB	n/a	24 TB
shared-network-prod	41 TB	n/a	33 TB
investments-prod	59 TB	n/a	6.6 TB

Links for the migration: how fast the data can move

Today you have 2 × 10 Gbps of Direct Connect (Equinix LD4 - LD6), costing $3.2k a month in ports and carrying 272 TB out last month. Those carry production traffic and stay as they are. The migration gets its own new 10 Gbps links, dedicated to the copy and kept apart from production, so moving 2.7 PB cannot slow customer-facing systems. Time assumes half the line rate is usable.

Option	New links	Time to copy	AWS ports	Data out	Total
Cheap Lowest cost; the copy takes longest.	1 × 10 Gbps	52 days	$4.9k	$56k	**$61k**
Medium Half the time of Cheap.	2 × 10 Gbps	26 days	$6.6k	$56k	**$63k**
Urgent Fastest: for a deadline or a stressed exit.	4 × 10 Gbps	13 days	$13k	$56k	**$69k**

- AWS list prices for Europe (London) (price list of 2026-10-13): $2.25 per 10 Gbps port-hour, paid for the copy plus 1 month to commission, test and run the final sync; data out over Direct Connect at $0.020 per GB on average, from the regions that hold the data. Data out costs the same whichever option you pick; the links only change how long it takes.
- Not included: your carrier's circuit and the cross-connect at the Direct Connect location. Enter them under Exit model to add them.
- Order early: a new dedicated connection needs a cross-connect at the Direct Connect location and a carrier circuit to your site, which often take weeks to months to deliver.
- AWS's price list also has flat-rate 10 Gbps ports with no per-GB charge, from $10.96 an hour in this region. For a one-off copy of this size, ask AWS whether one costs less than paying per GB.

8 Areas of focus: where the exit will be won or lost

The accounts whose complexity or risk needs attention, why, and how to tackle each one during the project. Derived from this scan with fixed rules, so the same scan always gives the same list; it does not change the score or the estimate. The AI's view is in the Agentic Risk Review, section 2.

Accounts to focus on
12
all shown below

Their share of the effort
77%
and 79% of spend (top 12)

AWS-only blockers
6
accounts with a Critical-tier service and no like-for-like target

Critical accounts
5
need a rehearsed cutover and fallback

Programme themes

Issues that cut across accounts and are cheaper to solve once.

- **The same services in many accounts** Mobilise
  In the most accounts, by effort: Lambda (10 accounts). Solving each once, as a pattern, is cheaper than solving it per account.
  How to tackle: Build a migration factory: a reference target, tooling and runbook per service, proven in one account, then reused. Most of the repeat discount in the estimate depends on it.

- **Critical-tier services set the critical path** Mobilise
  DynamoDB, Connect: no like-for-like target, so each needs a target decision (a product, or a redesign) before any build starts.
  How to tackle: Start each decision in the first quarter with the business owner: product selection, contracts, data-model redesign and retention rules usually take longer than the build.

- **2,742 TB of data to move** Mobilise
  Live and archived data across the estate. 13 to 52 days on new links.
  How to tackle: Order the links in mobilisation (carrier lead times run to months), and agree retention first: data that can be deleted or left archived does not need to move.

- **28 of 40 accounts have no owner** Before mobilisation
  $172k a month runs in accounts with no owner or executive tag.
  How to tackle: Tag an owner on every account (AWS Organizations tags) before planning waves; the wave plan is agreed with owners, not with accounts.

What to do when

The concerns below, by the project phase that should deal with them.

Phase	Deal with
Before mobilisation	**28 of 40 accounts have no owner** Name an accountable owner: search-prod, investments-prod Dependency scan before committing the plan: identity-prod, investments-prod
Mobilise	**The same services in many accounts** **Critical-tier services set the critical path** **2,742 TB of data to move** Decide the target for Critical-tier services: cards-processing-prod, payments-core-prod, contact-centre-prod, treasury-reporting-prod, fraud-analytics-prod, search-prod
Wave 1	Map and decouple AWS-only integrations: cards-processing-prod, treasury-reporting-prod Start the bulk data copy: cards-processing-prod, data-platform-prod, payments-core-prod, digital-channels-prod, core-banking-prod, ml-platform-prod, investments-prod
Wave 3	Dedicated squad, split into workloads: cards-processing-prod, data-platform-prod, contact-centre-prod, digital-channels-prod, fraud-analytics-prod, ml-platform-prod Re-architect (mostly AWS-only spend): data-platform-prod
Cutover	Rehearsed cutover and fallback: cards-processing-prod, payments-core-prod, digital-channels-prod, core-banking-prod, identity-prod

Accounts to focus on

Ranked by share of the effort, spend on AWS-only services and the weight of each concern.

1 cards-processing-prod Critical Wave 3

966773840736 · $101k a month · 228 engineer-weeks · Critical risk · Owner: Priya Shah

DynamoDB: no like-for-like target Mobilise

$35k a month on a Critical-tier service. Proprietary key-value/document model. Single-table designs, GSIs, conditional writes, TTL and DynamoDB Streams are baked into application code and data layout. No wire-compatible equivalent outside AWS. Typical duration 2-6 months per application.

How to tackle: Redesign the data access layer. Common targets are Cosmos DB, Firestore/Bigtable, ScyllaDB (Alternator offers a DynamoDB-compatible API) or PostgreSQL JSONB. Replace Streams consumers. Run dual-writes during cutover. Decide the target design during mobilisation: it is the long pole of this account.

536 AWS-only integrations Wave 1

536 integrations found by the dependency scan, 536 of them between AWS-only services (event sources, EventBridge targets, API Gateway, Step Functions).

How to tackle: Map the event flows with the team early, and put a portable messaging layer (Kafka, CloudEvents over HTTP) between producers and consumers before moving either side.

163 TB of data to move Wave 1

About 2 days of copy on one 10 Gbps link, before any change-data capture and validation.

How to tackle: Start the bulk copy early in the programme and keep it in sync with change-data capture, so the Wave 3 cutover only moves the last changes. Prune and archive first.

21% of the programme's effort Wave 3

About 228 engineer-weeks in this one account.

How to tackle: Give it a dedicated squad with the account's own engineers, and split it into workloads that can move separately.

Critical service Cutover

Marked critical (tag): an outage during cutover is a regulatory incident.

How to tackle: Move it last in its wave, after a rehearsed cutover and rollback; run in parallel until the target has passed a failover test, and agree the notification with the regulator up front.

2 data-platform-prod Wave 3

561017993421 · $133k a month · 151 engineer-weeks · High risk · Owner: Emma Botha

1,417 TB of data to move Wave 1

About 21 days of copy on one 10 Gbps link, before any change-data capture and validation.

How to tackle: Start the bulk copy early in the programme and keep it in sync with change-data capture, so the Wave 3 cutover only moves the last changes. Prune and archive first.

63% of spend on AWS-only services Wave 3

Mostly Redshift, Glue, QuickSight.

How to tackle: Treat it as a re-architecture, not a rehost: design the target first and prove it with one workload before planning the rest.

14% of the programme's effort Wave 3

About 151 engineer-weeks in this one account.

How to tackle: Give it a dedicated squad with the account's own engineers, and split it into workloads that can move separately.

3 payments-core-prod Critical Wave 3

534439589175 · $116k a month · 52 engineer-weeks · Low risk · Owner: Priya Shah

DynamoDB: no like-for-like target Mobilise

$3k a month on a Critical-tier service. Proprietary key-value/document model. Single-table designs, GSIs, conditional writes, TTL and DynamoDB Streams are baked into application code and data layout. No wire-compatible equivalent outside AWS. Typical duration 2-6 months per application.

How to tackle: Redesign the data access layer. Common targets are Cosmos DB, Firestore/Bigtable, ScyllaDB (Alternator offers a DynamoDB-compatible API) or PostgreSQL JSONB. Replace Streams consumers. Run dual-writes during cutover. Decide the target design during mobilisation: it is the long pole of this account.

216 TB of data to move Wave 1

About 3 days of copy on one 10 Gbps link, before any change-data capture and validation.

How to tackle: Start the bulk copy early in the programme and keep it in sync with change-data capture, so the Wave 3 cutover only moves the last changes. Prune and archive first.

Critical service Cutover

Marked critical (tag): an outage during cutover is a regulatory incident.

How to tackle: Move it last in its wave, after a rehearsed cutover and rollback; run in parallel until the target has passed a failover test, and agree the notification with the regulator up front.

4 contact-centre-prod Wave 3

125285552493 · $34k a month · 116 engineer-weeks · Critical risk · Owner: Lerato Mokoena

Connect: no like-for-like target Mobilise

$21k a month on a Critical-tier service. Full contact-centre platform - contact flows, phone numbers, Lex bots, Lambda integrations, recordings and agent desktop. Number porting and agent retraining make it a business transformation. Typical duration 6-12 months.

How to tackle: Select a CCaaS platform (Genesys, NICE, Five9, Dynamics 365 Contact Center), rebuild flows, port numbers, migrate recordings under retention rules, retrain agents. Decide the target design during mobilisation: it is the long pole of this account.

11% of the programme's effort Wave 3

About 116 engineer-weeks in this one account.

How to tackle: Give it a dedicated squad with the account's own engineers, and split it into workloads that can move separately.

5 digital-channels-prod Critical Wave 3

978681853473 · $57k a month · 71 engineer-weeks · Moderate risk · Owner: Lerato Mokoena

85 TB of data to move Wave 1

About a day or two of copy on one 10 Gbps link, before any change-data capture and validation.

How to tackle: Start the bulk copy early in the programme and keep it in sync with change-data capture, so the Wave 3 cutover only moves the last changes. Prune and archive first.

7% of the programme's effort Wave 3

About 71 engineer-weeks in this one account.

How to tackle: Give it a dedicated squad with the account's own engineers, and split it into workloads that can move separately.

Critical service Cutover

Marked critical (tag): an outage during cutover is a regulatory incident.

How to tackle: Move it last in its wave, after a rehearsed cutover and rollback; run in parallel until the target has passed a failover test, and agree the notification with the regulator up front.

6 treasury-reporting-prod Wave 3

499647302627 · $2.8k a month · 49 engineer-weeks · Critical risk · Owner: Thabo Dlamini

DynamoDB: no like-for-like target Mobilise

$1k a month on a Critical-tier service. Proprietary key-value/document model. Single-table designs, GSIs, conditional writes, TTL and DynamoDB Streams are baked into application code and data layout. No wire-compatible equivalent outside AWS. Typical duration 2-6 months per application.

How to tackle: Redesign the data access layer. Common targets are Cosmos DB, Firestore/Bigtable, ScyllaDB (Alternator offers a DynamoDB-compatible API) or PostgreSQL JSONB. Replace Streams consumers. Run dual-writes during cutover. Decide the target design during mobilisation: it is the long pole of this account.

58 AWS-only integrations Wave 1

58 integrations found by the dependency scan, 58 of them between AWS-only services (event sources, EventBridge targets, API Gateway, Step Functions).

How to tackle: Map the event flows with the team early, and put a portable messaging layer (Kafka, CloudEvents over HTTP) between producers and consumers before moving either side.

7 fraud-analytics-prod Wave 3

466806226017 · $20k a month · 57 engineer-weeks · High risk · Owner: Emma Botha

DynamoDB: no like-for-like target Mobilise

$3k a month on a Critical-tier service. Proprietary key-value/document model. Single-table designs, GSIs, conditional writes, TTL and DynamoDB Streams are baked into application code and data layout. No wire-compatible equivalent outside AWS. Typical duration 2-6 months per application.

How to tackle: Redesign the data access layer. Common targets are Cosmos DB, Firestore/Bigtable, ScyllaDB (Alternator offers a DynamoDB-compatible API) or PostgreSQL JSONB. Replace Streams consumers. Run dual-writes during cutover. Decide the target design during mobilisation: it is the long pole of this account.

5% of the programme's effort Wave 3

About 57 engineer-weeks in this one account.

How to tackle: Give it a dedicated squad with the account's own engineers, and split it into workloads that can move separately.

8 core-banking-prod Critical Wave 1

813958344723 · $122k a month · 26 engineer-weeks · Low risk · Owner: Thabo Dlamini

115 TB of data to move Wave 1

About a day or two of copy on one 10 Gbps link, before any change-data capture and validation.

How to tackle: Start the bulk copy early in the programme and keep it in sync with change-data capture, so the Wave 1 cutover only moves the last changes. Prune and archive first.

Critical service Cutover

Marked critical (tag): an outage during cutover is a regulatory incident.

How to tackle: Move it last in its wave, after a rehearsed cutover and rollback; run in parallel until the target has passed a failover test, and agree the notification with the regulator up front.

9 ml-platform-prod Wave 3

217230843944 · $47k a month · 58 engineer-weeks · Moderate risk · Owner: Emma Botha

123 TB of data to move Wave 1

About a day or two of copy on one 10 Gbps link, before any change-data capture and validation.

How to tackle: Start the bulk copy early in the programme and keep it in sync with change-data capture, so the Wave 3 cutover only moves the last changes. Prune and archive first.

5% of the programme's effort Wave 3

About 58 engineer-weeks in this one account.

How to tackle: Give it a dedicated squad with the account's own engineers, and split it into workloads that can move separately.

10 search-prod Wave 3

899894212661 · $4.0k a month · 23 engineer-weeks · Critical risk · No owner

No owner Before mobilisation

No owner or executive tag, so nobody is accountable for this account's move.

How to tackle: Name an accountable owner before mobilisation (and tag the account).

DynamoDB: no like-for-like target Mobilise

$1k a month on a Critical-tier service. Proprietary key-value/document model. Single-table designs, GSIs, conditional writes, TTL and DynamoDB Streams are baked into application code and data layout. No wire-compatible equivalent outside AWS. Typical duration 2-6 months per application.

How to tackle: Redesign the data access layer. Common targets are Cosmos DB, Firestore/Bigtable, ScyllaDB (Alternator offers a DynamoDB-compatible API) or PostgreSQL JSONB. Replace Streams consumers. Run dual-writes during cutover. Decide the target design during mobilisation: it is the long pole of this account.

11 **identity-prod** Critical — Wave 1

189183446249 · $7.9k a month · 8 engineer-weeks · Low risk · Owner: Thabo Dlamini

Sized from spend only Before mobilisation

One of the largest accounts, but no resource inventory was read, so its effort is the weakest figure in the plan.

How to tackle: Run a dependency scan on it (New scan, Dependency scan, only material accounts) before the plan is committed.

Critical service Cutover

Marked critical (tag): an outage during cutover is a regulatory incident.

How to tackle: Move it last in its wave, after a rehearsed cutover and rollback; run in parallel until the target has passed a failover test, and agree the notification with the regulator up front.

12 **investments-prod** Wave 1

514740085648 · $8.5k a month · 6 engineer-weeks · Low risk · No owner

Sized from spend only Before mobilisation

One of the largest accounts, but no resource inventory was read, so its effort is the weakest figure in the plan.

How to tackle: Run a dependency scan on it (New scan, Dependency scan, only material accounts) before the plan is committed.

No owner Before mobilisation

No owner or executive tag, so nobody is accountable for this account's move.

How to tackle: Name an accountable owner before mobilisation (and tag the account).

58 TB of data to move Wave 1

About a day or two of copy on one 10 Gbps link, before any change-data capture and validation.

How to tackle: Start the bulk copy early in the programme and keep it in sync with change-data capture, so the Wave 1 cutover only moves the last changes. Prune and archive first.

9 Data quality & scan issues

What this report does *not* cover. Every API error during the scan is recorded here and in the log.

Critical: 0 | Error: 0 | Warning: 2 | Info: 0

Severity	Area	Account	Issue
Warning	Inventory Ap-Southeast-2	data-platform-prod	Amazon EventBridge (events) in ap-southeast-2: Rate exceeded `ThrottlingException` → AWS throttled the request after retries. Re-run, or lower EXITRISK_MAX_WORKERS.
Warning	Catalog	n/a	'AWS Transform' is not in the service catalog; scored as Moderate (tier 3). $495/month in scope. → Add it to src/exitrisk/data/service_catalog.yaml (see CONTRIBUTING.md).

A Appendix: service exit-risk catalog

Every AWS service is classified into one of five tiers by how much of a workload must change to leave AWS. The tier sets the service's risk score; the recommended path and typical duration are for one workload of that service.

Tier	Score	Meaning
1 · Portable	10	Commodity infrastructure or an open standard. Lift-and-shift; config moves, code does not change.
2 · Low	30	Managed flavour of an open engine or de-facto standard API. Data and config migrate; little code change.
3 · Moderate	50	AWS-specific API with a close equivalent on every major cloud. Code changes at the integration points.
4 · High	75	Proprietary programming or data model. The workload must be redesigned, not just re-pointed.
5 · Critical	95	No equivalent outside AWS. Rebuild, re-platform or replace with a product; often a business change.

Tier 5 · Critical 3 services

Service	Why this tier	Recommended migration path	Equivalents	Typical duration
DynamoDB Database AI agent help: low $44k/mo in scope	Proprietary key-value/document model. Single-table designs, GSIs, conditional writes, TTL and DynamoDB Streams are baked into application code and data layout. No wire-compatible equivalent outside AWS.	Redesign the data access layer. Common targets are Cosmos DB, Firestore/Bigtable, ScyllaDB (Alternator offers a DynamoDB-compatible API) or PostgreSQL JSONB. Replace Streams consumers. Run dual-writes during cutover.	**Azure:** Cosmos DB **GCP:** Firestore / Bigtable / Spanner **Neutral:** ScyllaDB Alternator / Cassandra / PostgreSQL	2-6 months per application
Connect Business apps AI agent help: none $21k/mo in scope	Full contact-centre platform - contact flows, phone numbers, Lex bots, Lambda integrations, recordings and agent desktop. Number porting and agent retraining make it a business transformation.	Select a CCaaS platform (Genesys, NICE, Five9, Dynamics 365 Contact Center), rebuild flows, port numbers, migrate recordings under retention rules, retrain agents.	**Azure:** Dynamics 365 Contact Center **GCP:** Contact Center AI Platform **Neutral:** Genesys Cloud / NICE CXone / Five9	6-12 months
SWF Integration AI agent help: high $712/mo in scope	Legacy proprietary workflow engine with a bespoke decider/worker model; no equivalent.	Rewrite on Temporal (the conceptual successor) or Durable Functions.	**Azure:** Durable Functions **GCP:** Workflows **Neutral:** Temporal	2-4 months

Tier 4 · High 16 services

Service	Why this tier	Recommended migration path	Equivalents	Typical duration
Redshift Analytics AI agent help: low $62k/mo in scope	PostgreSQL-derived but proprietary MPP warehouse - distribution/sort keys, Spectrum external tables, stored procedures, UNLOAD/COPY from S3, Redshift ML and data sharing are all specific. Downstream BI and ELT jobs depend on its dialect.	Choose a warehouse (Snowflake or Databricks are cloud-neutral; BigQuery / Fabric Warehouse are native). Convert DDL and SQL with a translation tool, re-point ELT (dbt makes this far cheaper), reconcile results in parallel for several reporting cycles.	**Azure:** Fabric Warehouse / Synapse / Snowflake **GCP:** BigQuery **Neutral:** Snowflake / Databricks / ClickHouse	3-9 months per warehouse
Lambda Compute AI agent help: high $33k/mo in scope	The function code is portable, but the event model, triggers (S3, SQS, DynamoDB streams, EventBridge), IAM wiring, layers and runtime limits are AWS-specific. Real Lambda estates are mostly glue between other AWS services.	Inventory triggers first. Repackage as containers on Cloud Run / Container Apps / Knative, or rewrite as Azure Functions; replace each event source with the target's equivalent. Migrate with the services it glues together, not alone.	**Azure:** Azure Functions / Container Apps **GCP:** Cloud Run functions **Neutral:** Knative / OpenFaaS on Kubernetes	4-12 weeks per application
Glue Analytics AI agent help: high $15k/mo in scope	Spark under the hood, but jobs use GlueContext/DynamicFrame APIs, the Glue Data Catalog, crawlers and Glue workflows. The catalog is usually shared by Athena, EMR, Redshift Spectrum and Lake Formation, so it is a hub.	Port jobs to plain Spark (Databricks, Dataproc, Synapse Spark), migrate the catalog to Unity / Hive Metastore / Dataplex, and replace crawlers with explicit schemas.	**Azure:** Data Factory + Databricks **GCP:** Dataproc / Dataflow + Dataplex **Neutral:** Spark + Airflow + Hive Metastore	1-4 months
Kinesis Streams Analytics AI agent help: medium $9.7k/mo in scope	Proprietary streaming API (shards, KCL checkpointing in DynamoDB, enhanced fan-out). Producers and consumers must be rewritten.	Move to Kafka (MSK-equivalent, Confluent, Event Hubs Kafka endpoint) or Pub/Sub; rewrite producers/consumers against the Kafka API to avoid the next lock-in.	**Azure:** Event Hubs (Kafka API) **GCP:** Pub/Sub / Managed Kafka **Neutral:** Apache Kafka / Redpanda	1-3 months
Cognito Security AI agent help: medium $8.0k/mo in scope	User pools hold customer identities; password hashes cannot be exported, and triggers / hosted UI are AWS-specific. Customers notice an identity migration.	Move to Entra External ID, Identity Platform, Auth0 or Keycloak using lazy (on-login) migration; plan MFA re-enrolment and app token changes.	**Azure:** Entra External ID **GCP:** Identity Platform **Neutral:** Auth0 / Keycloak / Okta CIC	2-4 months (customer-facing)
Step Functions Integration AI agent help: high $7.4k/mo in scope	Workflows are written in Amazon States Language with direct service integrations to 200+ AWS APIs; nothing executes ASL outside AWS.	Rewrite workflows in Logic Apps / Durable Functions, Google Workflows, or Temporal (cloud-neutral and code-first). Redesign each service integration step.	**Azure:** Logic Apps / Durable Functions **GCP:** Workflows **Neutral:** Temporal / Argo Workflows	1-3 months
QuickSight Analytics AI agent help: medium $5.9k/mo in scope	Proprietary BI tool; dashboards, SPICE datasets and embedding cannot be exported to other BI products.	Rebuild priority dashboards in Power BI, Looker or Superset; retire the long tail. Treat as a business change, not a technical migration.	**Azure:** Power BI **GCP:** Looker **Neutral:** Apache Superset / Tableau	1-3 months

Service	Why this tier	Recommended migration path	Equivalents	Typical duration
AppSync Integration AI agent help: high $4.3k/mo in scope	GraphQL is standard but AppSync resolvers (VTL / APPSYNC_JS), data-source bindings and subscriptions are proprietary.	Re-implement with Apollo Server / Hasura / Azure API Management GraphQL; rewrite resolvers.	**Azure:** API Management (GraphQL) / Hasura **GCP:** Apollo on Cloud Run **Neutral:** Apollo / Hasura	1-3 months
Lex AI/ML AI agent help: medium $3.1k/mo in scope	Proprietary bot definitions, intents and Connect integration.	Rebuild bots in Copilot Studio / Dialogflow CX or an LLM-based assistant.	**Azure:** Copilot Studio **GCP:** Dialogflow CX **Neutral:** Rasa / LLM agents	1-3 months
Pinpoint Business apps AI agent help: medium $2.8k/mo in scope	Proprietary campaign, journey and segment definitions; sender IDs and registered numbers are tied to AWS. AWS ends support for Pinpoint's engagement features (campaigns, journeys, segments, analytics) on 30 October 2026; SMS, voice and push continue as AWS End User Messaging.	Move to Braze / Twilio / Azure Communication Services, or within AWS to Connect outbound campaigns; re-register sender IDs and short codes.	**Azure:** Azure Communication Services **GCP:** Firebase Cloud Messaging + partner **Neutral:** Braze / Twilio	1-3 months
Timestream Database AI agent help: medium $2.0k/mo in scope	Proprietary time-series engine and SQL dialect (Timestream for InfluxDB is the portable variant).	Move to InfluxDB, TimescaleDB, Azure Data Explorer or Bigtable; rewrite queries and ingestion.	**Azure:** Azure Data Explorer **GCP:** Bigtable / BigQuery **Neutral:** InfluxDB / TimescaleDB	1-3 months
EventBridge Integration AI agent help: high $1.7k/mo in scope	Proprietary event bus whose value is AWS-native event sources, rules, Pipes and the Scheduler. Event patterns and targets are AWS ARNs.	Re-implement routing on Event Grid / Eventarc or Kafka; replace AWS-native sources with the target's audit/event feeds; move schedules to the target scheduler.	**Azure:** Event Grid **GCP:** Eventarc / Cloud Scheduler **Neutral:** Kafka / Argo Events	1-2 months
Amplify DevOps AI agent help: high $1.3k/mo in scope	Opinionated framework that generates Cognito, AppSync, DynamoDB and Lambda backends; front-end hosting is portable, the generated backend is not.	Host front-ends on Static Web Apps / Firebase Hosting / Vercel; re-platform the backend along with Cognito, AppSync and DynamoDB.	**Azure:** Static Web Apps **GCP:** Firebase Hosting **Neutral:** Vercel / Netlify	1-3 months
Bedrock AgentCore AI/ML AI agent help: medium $1.2k/mo in scope	Agent runtime, memory, gateway, identity and observability services with AWS-specific APIs. Agent code written with open frameworks is portable; the hosting, memory stores and tool gateway are not.	Keep agent logic in an open framework (LangGraph, Strands, Claude Agent SDK); re-host on Azure AI Foundry Agent Service, Vertex AI Agent Engine or containers; migrate memory to a vector/relational store you control.	**Azure:** Azure AI Foundry Agent Service **GCP:** Vertex AI Agent Engine **Neutral:** Containers + open agent frameworks	1-2 months
Lake Formation Analytics AI agent help: medium $640/mo in scope	Proprietary fine-grained permission layer over the Glue catalog; access policies must be re-modelled.	Re-implement as Unity Catalog, Microsoft Purview / OneLake security, or Dataplex policies.	**Azure:** Microsoft Purview / OneLake security **GCP:** Dataplex / BigLake **Neutral:** Unity Catalog / Apache Ranger	1-2 months
Data Pipeline Analytics AI agent help: high $327/mo in scope	Legacy proprietary orchestration (in maintenance mode).	Rewrite as Airflow DAGs or Data Factory pipelines.	**Azure:** Data Factory **GCP:** Cloud Composer **Neutral:** Apache Airflow	1-2 months

Tier 3 · Moderate 10 services

Service	Why this tier	Recommended migration path	Equivalents	Typical duration
SageMaker AI/ML AI agent help: medium $23k/mo in scope	Models (PyTorch, XGBoost, Hugging Face) and containers are portable, but pipelines, feature store, endpoints and Studio domains are SageMaker-specific.	Move training/inference to Azure ML / Vertex AI or Kubeflow/MLflow; rebuild pipelines and feature store.	**Azure:** Azure Machine Learning **GCP:** Vertex AI **Neutral:** Kubeflow / MLflow / KServe	1-3 months
API Gateway Integration AI agent help: high $11k/mo in scope	OpenAPI definitions export, but Lambda/VTL integrations, authorizers, usage plans and WebSocket routes are AWS-specific.	Export OpenAPI, re-implement on Azure API Management, Apigee or Kong; rewrite authorizers and mapping templates.	**Azure:** API Management **GCP:** Apigee / API Gateway **Neutral:** Kong / Envoy Gateway	3-8 weeks
Bedrock AI/ML AI agent help: medium $7.6k/mo in scope	Foundation models (Anthropic Claude, Llama, Mistral) are available on other clouds and direct from providers, but Bedrock Agents, Knowledge Bases, Guardrails and Flows are proprietary orchestration.	Call the same models via Vertex AI / Azure AI Foundry or the provider's own API; re-implement agents and RAG pipelines with a portable framework; re-run evaluations.	**Azure:** Azure AI Foundry **GCP:** Vertex AI **Neutral:** Provider APIs (Anthropic	3-8 weeks
Neptune Database AI agent help: low $6.8k/mo in scope	Graph database using open query languages (Gremlin, openCypher, SPARQL), but loaders, IAM auth and Neptune-specific extensions need rework.	Move to Neo4j, Cosmos DB for Gremlin or JanusGraph; re-validate query behaviour.	**Azure:** Cosmos DB for Apache Gremlin **GCP:** Neo4j AuraDB / Spanner Graph **Neutral:** Neo4j / JanusGraph	1-3 months
Athena Analytics AI agent help: high $6.6k/mo in scope	Trino/Presto-based SQL, so queries are largely portable, but it is bound to the Glue Data Catalog, S3 locations and Athena workgroups.	Move tables to Iceberg/Delta, query with Trino, BigQuery or Databricks SQL.	**Azure:** Fabric / Synapse serverless SQL **GCP:** BigQuery **Neutral:** Trino / Starburst	3-8 weeks
SQS Integration AI agent help: high $3.6k/mo in scope	Simple semantics, but a proprietary API; every producer and consumer needs a code change.	Move to Service Bus / Pub/Sub / RabbitMQ behind a small messaging abstraction; drain queues at cutover.	**Azure:** Service Bus / Storage Queues **GCP:** Pub/Sub / Cloud Tasks **Neutral:** RabbitMQ / NATS	2-6 weeks

Service	Why this tier	Recommended migration path	Equivalents	Typical duration
Transcribe AI/ML AI agent help: medium $3.4k/mo in scope	Proprietary speech API; custom vocabularies need recreating.	Swap to Azure AI Speech / Speech-to-Text or Whisper.	**Azure:** Azure AI Speech **GCP:** Speech-to-Text **Neutral:** Whisper	2-4 weeks
Textract AI/ML AI agent help: medium $3.0k/mo in scope	Proprietary document-extraction API and output schema.	Move to Azure Document Intelligence / Document AI; re-map output parsing and re-validate accuracy.	**Azure:** Document Intelligence **GCP:** Document AI **Neutral:** Open-source OCR + LLM extraction	1-2 months
Firehose Analytics AI agent help: medium $2.6k/mo in scope	Managed delivery pipeline with AWS-only sources and destinations.	Replace with Kafka Connect, Event Hubs Capture, or Dataflow templates.	**Azure:** Event Hubs Capture / Stream Analytics **GCP:** Dataflow / Pub/Sub subscriptions **Neutral:** Kafka Connect / Vector	3-6 weeks
SNS Integration AI agent help: high $1.8k/mo in scope	Proprietary pub/sub and SMS/mobile push API, usually fanned out to SQS and Lambda.	Move topics to Event Grid / Service Bus topics / Pub/Sub; move SMS to a CPaaS provider (Twilio, Azure Communication Services).	**Azure:** Event Grid / Service Bus topics **GCP:** Pub/Sub **Neutral:** NATS / Kafka + Twilio	2-6 weeks

Tier 2 · Low 18 services

Service	Why this tier	Recommended migration path	Equivalents	Typical duration
RDS / Aurora Database AI agent help: low $107k/mo in scope	PostgreSQL, MySQL, MariaDB, SQL Server and Oracle engines, plus Aurora (PostgreSQL/MySQL compatible). Schemas and SQL move; Aurora-only features (Global Database, Babelfish, Aurora Serverless scaling, IAM DB auth) and Oracle/SQL Server licensing need attention.	Migrate with native replication or DMS-equivalents (Azure DMS, Database Migration Service) into Azure Database / Cloud SQL / AlloyDB. Cut over per database with a short read-only window.	**Azure:** Azure Database for PostgreSQL/MySQL / Azure SQL **GCP:** Cloud SQL / AlloyDB **Neutral:** Self-managed PostgreSQL (CloudNativePG)	2-8 weeks per database
S3 Storage AI agent help: low $55k/mo in scope	The S3 API is a de-facto standard implemented by most object stores, but bucket policies, event notifications, lifecycle rules, Object Lock and presigned URL patterns need translating, and large data sets incur egress cost and transfer time.	Copy with rclone / Storage Transfer Service / AzCopy; use S3-compatible endpoints where code depends on the S3 SDK; recreate lifecycle, retention and event rules.	**Azure:** Blob Storage **GCP:** Cloud Storage **Neutral:** MinIO / Ceph RGW	1-8 weeks (data-volume bound)
ECS Compute AI agent help: high $14k/mo in scope	Containers are portable but ECS task definitions, service discovery and deployment wiring are AWS-specific and must be rewritten.	Convert task definitions to Kubernetes manifests or Azure Container Apps / Cloud Run definitions. Images move unchanged.	**Azure:** Container Apps / AKS **GCP:** Cloud Run / GKE **Neutral:** Kubernetes / Nomad	2-6 weeks per service group
Direct Connect Networking AI agent help: none $11k/mo in scope	Physical circuits; lead times for new carrier connections dominate.	Order ExpressRoute / Cloud Interconnect early (8-16 week lead time is common).	**Azure:** ExpressRoute **GCP:** Cloud Interconnect **Neutral:** Carrier MPLS	2-4 months (carrier lead time)
EMR Analytics AI agent help: medium $11k/mo in scope	Open-source Spark, Hive, Presto, Flink. EMRFS, bootstrap actions and step orchestration need adjusting.	Run the same jobs on Databricks, Dataproc or HDInsight; swap s3:// paths and IAM roles.	**Azure:** Databricks / HDInsight **GCP:** Dataproc **Neutral:** Spark on Kubernetes	1-2 months
Marketplace (3rd party) Third-party software AI agent help: none $9.2k/mo in scope	Third-party software bought through AWS billing. The product usually exists on other clouds or direct from the vendor; contracts and private offers need re-papering.	Re-contract directly or via the target cloud's marketplace; align with contract renewal dates.	**Azure:** Azure Marketplace **GCP:** Google Cloud Marketplace **Neutral:** Direct vendor contract	Contract-bound
CloudWatch Management AI agent help: high $8.4k/mo in scope	Metrics, logs, alarms and dashboards are re-creatable, but Embedded Metric Format, Logs Insights queries and alarm-driven automation are AWS-specific.	Standardise on OpenTelemetry and ship to Azure Monitor / Cloud Monitoring / Grafana stack; rebuild alarms and dashboards from code.	**Azure:** Azure Monitor **GCP:** Cloud Monitoring / Logging **Neutral:** Grafana / Prometheus / Loki / Datadog	2-4 weeks
CloudFront Networking AI agent help: medium $7.4k/mo in scope	A CDN like any other, but Lambda@Edge / CloudFront Functions and signed-URL schemes are proprietary.	Move to Front Door, Cloud CDN, Cloudflare or Akamai; rewrite edge functions.	**Azure:** Front Door **GCP:** Cloud CDN **Neutral:** Cloudflare / Akamai / Fastly	1-3 weeks
Network Firewall Networking AI agent help: medium $5.3k/mo in scope	Suricata-compatible rules; policy structure is AWS-specific.	Translate rules to Azure Firewall / Cloud NGFW or a vendor NGFW.	**Azure:** Azure Firewall **GCP:** Cloud NGFW **Neutral:** Palo Alto / Fortinet	2-4 weeks
Managed Flink Analytics AI agent help: high $3.6k/mo in scope	Apache Flink applications are portable; legacy Kinesis SQL applications are not.	Run Flink jobs on Confluent, Ververica, or Flink on Kubernetes; rewrite any legacy SQL apps.	**Azure:** Flink on HDInsight on AKS / Stream Analytics **GCP:** Dataflow / Flink on GKE **Neutral:** Apache Flink	1-2 months
Backup Storage AI agent help: low $3.4k/mo in scope	Backup policies and vaults are AWS-specific; the protected data moves with each workload. Retained backups must be kept (or restored and re-protected) to meet retention obligations.	Recreate policies in Azure Backup / Backup and DR; keep the AWS vault read-only until retention expires.	**Azure:** Azure Backup **GCP:** Backup and DR **Neutral:** Veeam / Commvault	Retention-bound tail

Service	Why this tier	Recommended migration path	Equivalents	Typical duration
KMS Security AI agent help: none $2.4k/mo in scope	Keys cannot be exported from KMS. Data encrypted under KMS must be decrypted and re-encrypted on the target; envelope-encryption code calls the KMS API.	Create keys in Key Vault / Cloud KMS (or an external HSM / BYOK), re-encrypt data during migration, swap the SDK calls.	**Azure:** Key Vault / Managed HSM **GCP:** Cloud KMS / Cloud HSM **Neutral:** HashiCorp Vault / Thales HSM	Moves with the workload
Directory Service Security AI agent help: medium $2.2k/mo in scope	Managed Microsoft AD - standard Active Directory.	Extend trusts to Entra Domain Services / Managed AD on the target and migrate members.	**Azure:** Entra Domain Services **GCP:** Managed Service for Microsoft AD **Neutral:** Active Directory	1-2 months
ACM / Private CA Security AI agent help: low $1.6k/mo in scope	Public certificates are free to reissue elsewhere; a private CA hierarchy must be re-established and trusted by every client.	Reissue public certs on the target; plan a private CA trust rollout (or adopt a cloud-neutral CA such as Vault PKI).	**Azure:** Key Vault certificates **GCP:** Certificate Authority Service **Neutral:** Vault PKI / EJBCA	2-6 weeks
WAF Security AI agent help: medium $1.5k/mo in scope	Rule concepts are common; rule syntax and managed rule groups are AWS-specific.	Translate rules to Azure WAF / Cloud Armor / Cloudflare WAF; re-tune in detection mode before enforcing.	**Azure:** Azure WAF **GCP:** Cloud Armor **Neutral:** Cloudflare / Akamai WAF	2-4 weeks
Global Accelerator Networking AI agent help: medium $766/mo in scope	Anycast IP front door; static IPs cannot be moved.	Replace with Front Door / global load balancer; plan for client IP allow-list changes.	**Azure:** Front Door / cross-region Load Balancer **GCP:** Global external Load Balancer **Neutral:** Cloudflare Spectrum	2-4 weeks
Secrets Manager Security AI agent help: medium $647/mo in scope	Simple secret store, but rotation Lambdas and SDK calls are AWS-specific.	Move secrets to Key Vault / Secret Manager / Vault; rewrite rotation; prefer External Secrets Operator for Kubernetes workloads.	**Azure:** Key Vault **GCP:** Secret Manager **Neutral:** HashiCorp Vault	1-2 weeks
Batch Compute AI agent help: high $0/mo in scope	Container jobs on EC2/Fargate; job definitions and queues are AWS-specific.	Move to Azure Batch, Google Batch, or Kubernetes Jobs / Argo Workflows.	**Azure:** Azure Batch **GCP:** Google Batch **Neutral:** Kubernetes Jobs / Slurm	2-4 weeks

Tier 1 · Portable 12 services

Service	Why this tier	Recommended migration path	Equivalents	Typical duration
EC2 Compute AI agent help: low $188k/mo in scope	Virtual machines running standard operating systems. Images can be exported or rebuilt from configuration management.	Rehost VMs (Azure Migrate, Google Migrate to VMs, or rebuild from Packer/Ansible images). Re-baseline instance sizes on the target.	**Azure:** Virtual Machines **GCP:** Compute Engine **Neutral:** VMware / OpenStack / bare metal	1-4 weeks per application
EC2 Other (EBS, NAT, transfer) Compute AI agent help: low $43k/mo in scope	Block storage, snapshots, NAT gateways, elastic IPs and data transfer. Commodity primitives on every cloud.	Recreate volumes and network egress on the target; move data with snapshots or block replication. Budget for one-off egress charges.	**Azure:** Managed Disks / NAT Gateway **GCP:** Persistent Disk / Cloud NAT **Neutral:** SAN / Ceph	Moves with the workload
EKS Compute AI agent help: medium $14k/mo in scope	Upstream Kubernetes. Manifests and Helm charts run on any conformant cluster; AWS-specific add-ons (IRSA, ALB controller, EBS CSI) are small and swappable.	Stand up AKS/GKE/on-prem Kubernetes, swap cloud add-ons (identity, ingress, storage classes), redeploy via GitOps.	**Azure:** AKS **GCP:** GKE **Neutral:** OpenShift / Rancher / upstream Kubernetes	2-6 weeks per cluster
VPC Networking AI agent help: medium $12k/mo in scope	Standard network constructs (subnets, routing, VPN, IPAM); only the console and APIs differ.	Design the target landing-zone network; reuse the IP plan where possible.	**Azure:** Virtual Network **GCP:** VPC **Neutral:** Data-centre networking	Part of landing zone
MSK (Kafka) Analytics AI agent help: low $7.9k/mo in scope	Standard Apache Kafka.	Mirror topics with MirrorMaker 2 / Cluster Linking and cut consumers over.	**Azure:** Event Hubs (Kafka) / Confluent **GCP:** Managed Service for Apache Kafka **Neutral:** Apache Kafka / Redpanda	2-6 weeks
FSx Storage AI agent help: none $5.7k/mo in scope	Managed Windows File Server, Lustre, ONTAP or OpenZFS - all standard file systems.	Replicate to the equivalent managed file system (ONTAP SnapMirror where applicable).	**Azure:** Azure Files / NetApp Files **GCP:** Filestore / NetApp Volumes **Neutral:** NetApp / Windows File Server	2-4 weeks
OpenSearch Analytics AI agent help: low $4.7k/mo in scope	Open-source OpenSearch / Elasticsearch APIs (Serverless collections have a reduced API).	Snapshot/restore or reindex into Elastic Cloud, OpenSearch on Kubernetes or Azure AI Search where suitable.	**Azure:** Elastic Cloud on Azure **GCP:** Elastic Cloud on GCP **Neutral:** OpenSearch	2-4 weeks
ELB Networking AI agent help: medium $4.2k/mo in scope	Standard L4/L7 load balancing.	Recreate listeners and rules on Application Gateway / Cloud Load Balancing / Envoy.	**Azure:** Load Balancer / Application Gateway **GCP:** Cloud Load Balancing **Neutral:** HAProxy / F5 / Envoy	Moves with the workload
ElastiCache Database AI agent help: low $4.2k/mo in scope	Managed Redis / Valkey / Memcached - open engines.	Provision the target cache and warm it; caches rarely need data migration.	**Azure:** Azure Cache for Redis **GCP:** Memorystore **Neutral:** Redis / Valkey	Days

Service	Why this tier	Recommended migration path	Equivalents	Typical duration
MWAA (Airflow) Analytics AI agent help: medium $2.0k/mo in scope	Apache Airflow; DAGs are portable apart from AWS operators.	Move DAGs to Cloud Composer, Astronomer or Airflow on Kubernetes; swap AWS operators.	**Azure:** Data Factory Workflow Orchestration Manager / Astronomer **GCP:** Cloud Composer **Neutral:** Apache Airflow	2-4 weeks
Amazon MQ Integration AI agent help: low $1.4k/mo in scope	Managed ActiveMQ / RabbitMQ - standard protocols (AMQP, MQTT, STOMP, JMS).	Shovel/federate queues to the target broker and cut clients over.	**Azure:** Service Bus (AMQP) / RabbitMQ on AKS **GCP:** RabbitMQ on GKE **Neutral:** RabbitMQ / ActiveMQ	1-3 weeks
Route 53 Networking AI agent help: medium $991/mo in scope	DNS zones export as standard zone files. Alias records, health-check routing and Resolver rules need translating.	Export zones, recreate in Azure DNS / Cloud DNS / NS1, then lower TTLs and switch NS records.	**Azure:** Azure DNS **GCP:** Cloud DNS **Neutral:** NS1 / Cloudflare DNS	1-2 weeks

Unclassified services in this estate

Scored as Moderate (tier 3) until added to the catalog.

- AWS Transform: $495/month

B Appendix: methodology

Data sources

Spend comes from AWS Cost Explorer in the management (payer) account: amortised cost per account per service per month, excluding tax, credits, refunds and support. Marketplace purchases are grouped as one third-party line. Accounts and OU structure come from AWS Organizations. The optional deep scan counts resources (Lambda functions, DynamoDB tables, state machines, stacks and more) in each member account through a read-only role. All API calls are read-only.

Scoring

Each service's tier maps to a score: Portable 10, Low 30, Moderate 50, High 75, Critical 95. An account's **inherent risk** is the spend-weighted average of its services' scores.

The report gives **two OU scores**. **By spend** weights each account by its share of in-scope spend, so a small account full of proprietary services scores high on its own yet moves the score very little. **By number of accounts** counts every account with spend equally, so one large account (for example a contact centre on Connect) cannot dominate it. A gap between the two shows whether risk is concentrated in a few big accounts or spread across many. An account's **contribution** is its inherent risk × its weight under the weighting chosen in the bar at the top (by spend unless changed).

Ratings: Low < 25 ≤ Moderate < 40 ≤ Elevated < 55 ≤ High < 70 ≤ Critical.

Estimate

The cost and time figures depend on the delivery questions under Exit model. Until they are answered, the report marks the figures provisional and keeps them out of the bottom line.

Effort is built bottom-up: each material service in each account contributes the catalog's engineer-weeks for one workload, scaled by the square root of its spend relative to US$1,000/month (and by its resource count where the deep scan ran). Data migration effort (per TB moved and per account holding data), account overhead, a target landing zone, programme management and contingency are added, and the total is adjusted for delivery maturity from the questionnaire. Duration is the longest of effort ÷ available capacity (with a ramp-up), the critical path of the hardest tier present, and the data path: ordering links, the bulk copy and the final cutover. Cost adds parallel running and the target platform while the exit runs. The range around each figure is widest on billing data alone and narrows once deep and dependency scans have run.

Limitations

- Spend is a proxy for size; a cheap service can still be hard to move (the deep scan's resource counts partly correct for this).
- RDS spend covers all engines; Aurora-specific features and commercial engines (Oracle, SQL Server) appear in the deep scan's engine breakdown.
- Contractual exit costs (EDP commitments, Savings Plans, Reserved Instances) and target-cloud run costs are outside the estimate; commitments still owed after the exit are shown separately, as written off, under Timing.
- The estimate is an order-of-magnitude planning figure for an executive decision, not a delivery quote.
